ID	Task Name
1	finish TDR
2	Lehman review
3	DOE decides it wants ILC
4	Money available
5	CFS contract negociations/bids
6	civil construction starts
7	
8	Finish RDR
9	
10	
11	
12	**Site specific work**
13	RFP for A&E firm
14	AE/CM Selection
15	Develop siting criteria
16	Conceptual design
17	Site characterizations
18	Identification of specific sit
19	Public Outreach on site
20	Preliminary NEPA docume
21	
22	International Evaluation of Bid-t
23	international site decision
24	preliminary civil design (title 1)
25	final civil design (title 2)
26	
27	
28	schedule start date
29	S0 (prove 35 MeV/m high yield
30	
31	S1 (build 3 31.5 Mev/m cryomo
32	
33	S2 phase 1 (3 RF units?) const
34	S2 phase 1 testing
35	S2 phase 2 (6 more RF units?)
36	S2 phase 2 testing

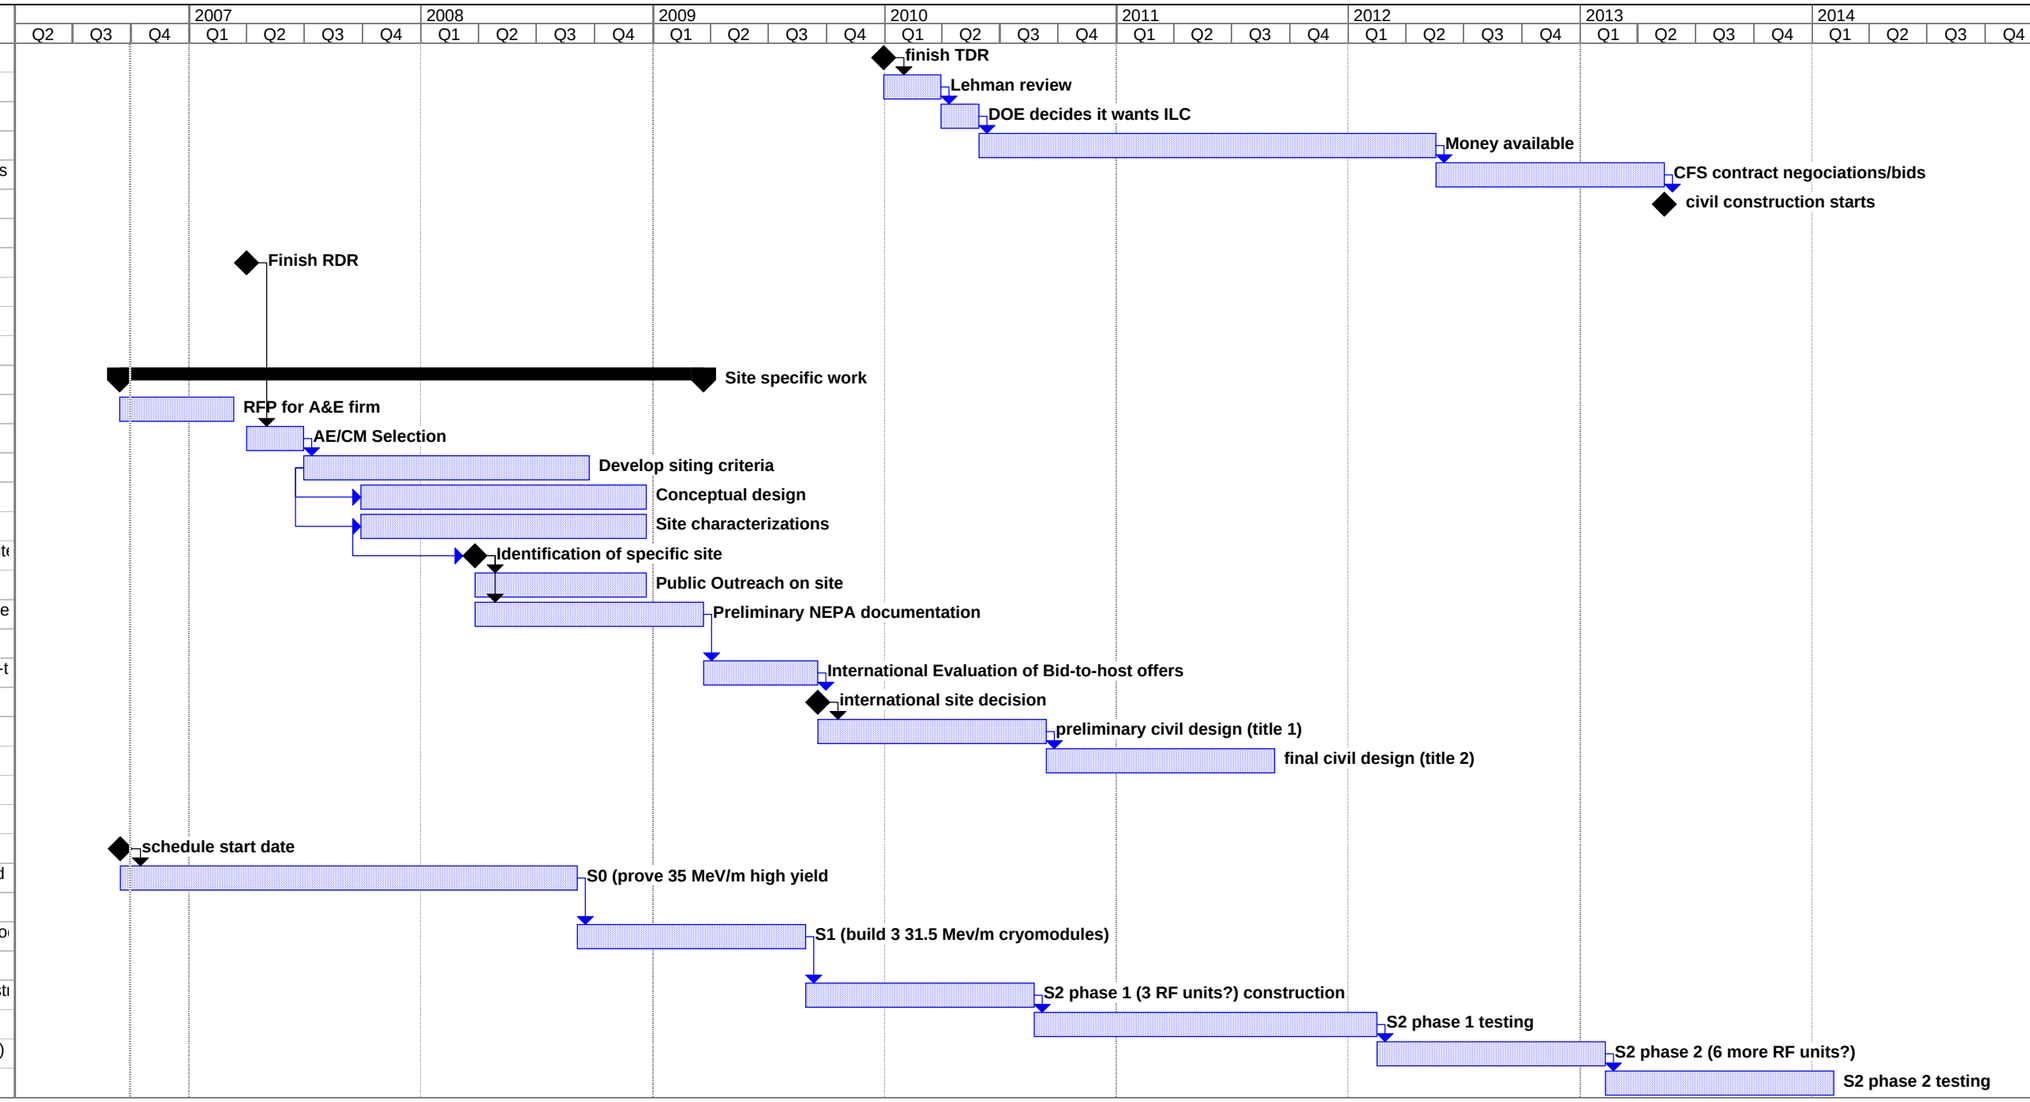

Project: ILC overview~843
Date: Fri 9/29/06

Task		Milestone		Rolled Up Task		Rolled Up Progress		External Tasks		Group By Summary	
Progress		Summary		Rolled Up Milestone		Split		Project Summary		Deadline	
